



Post

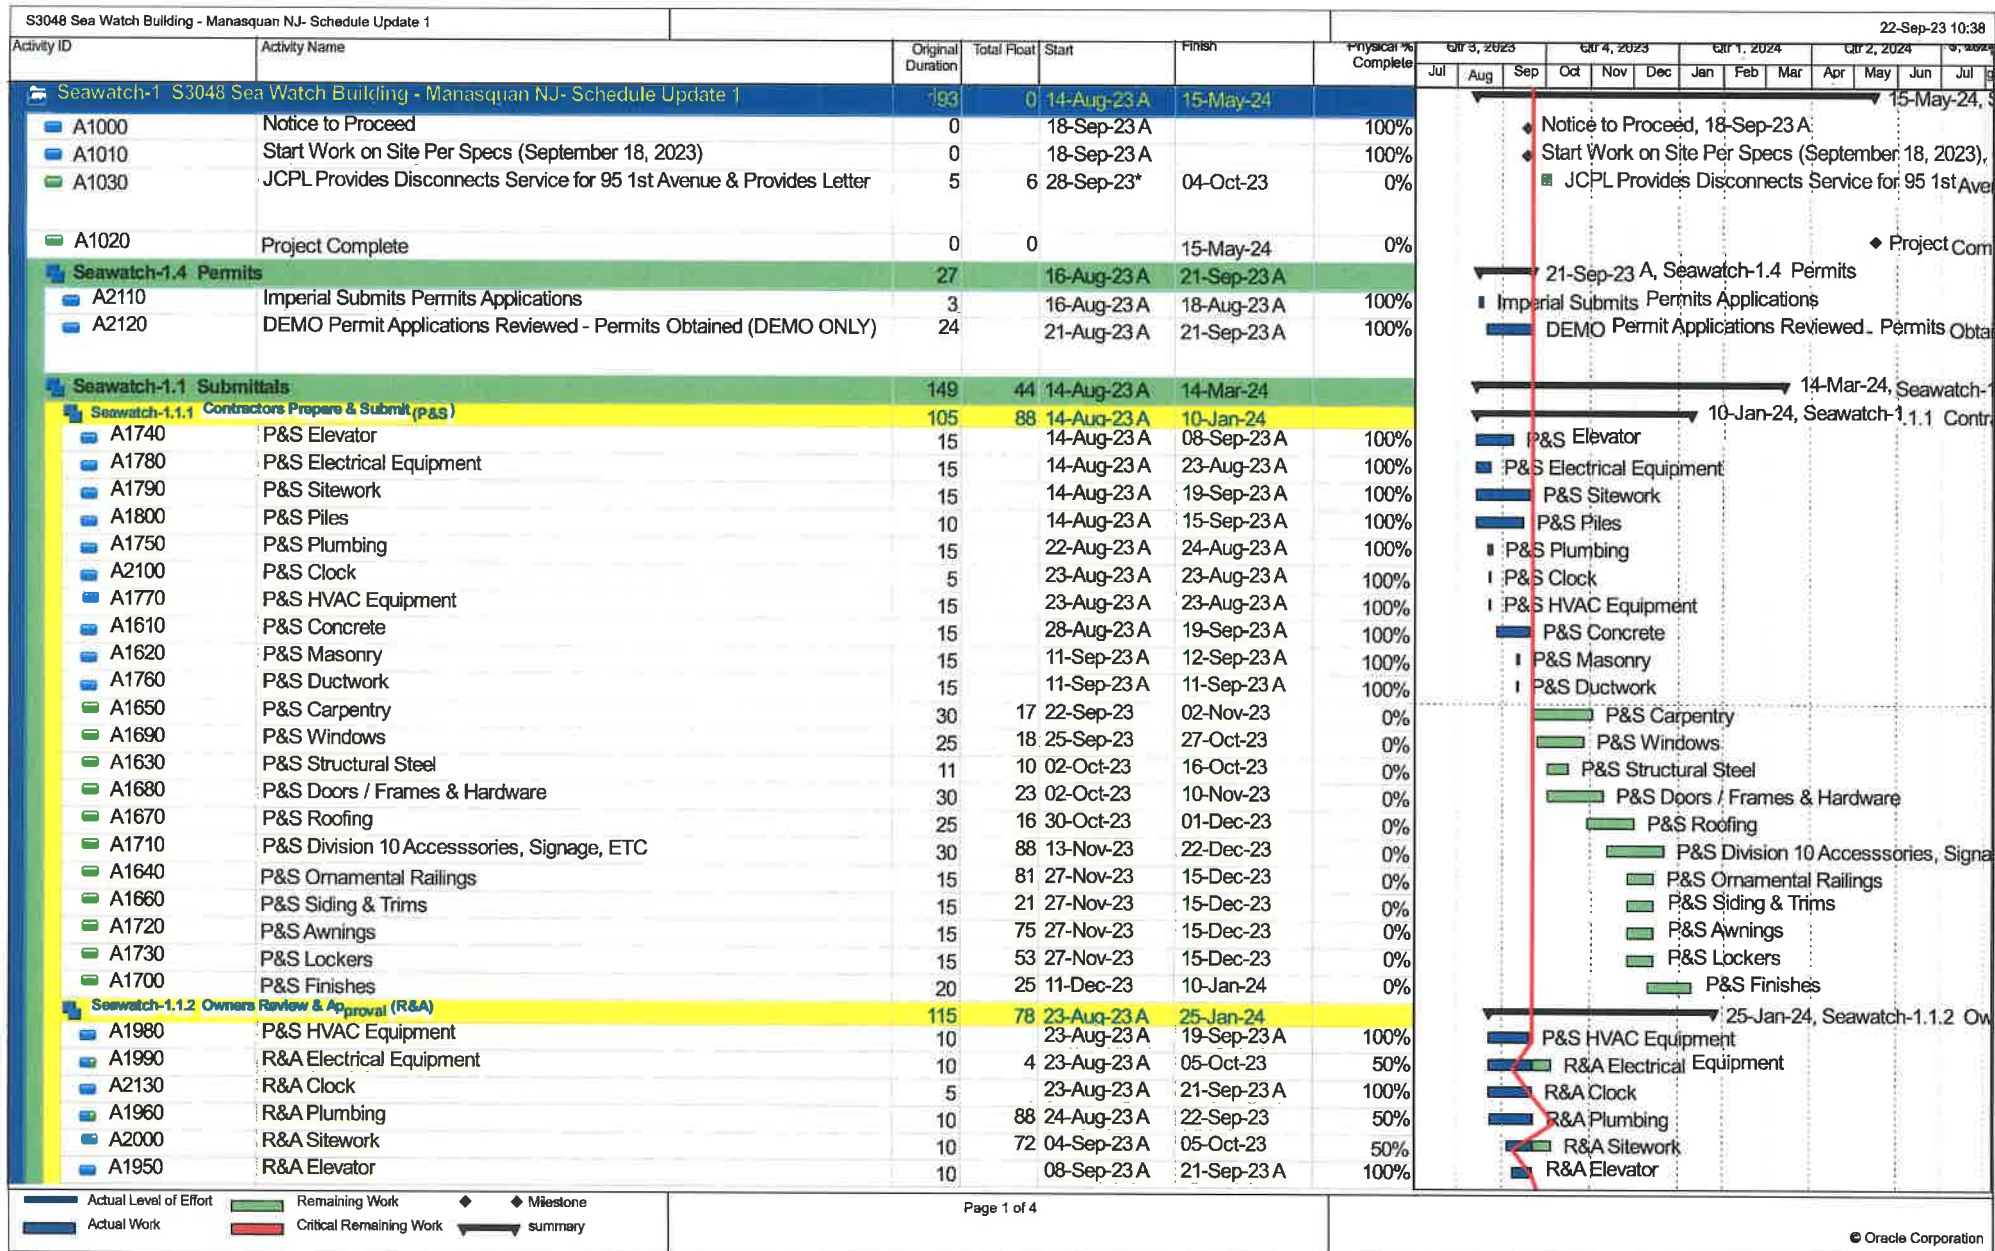

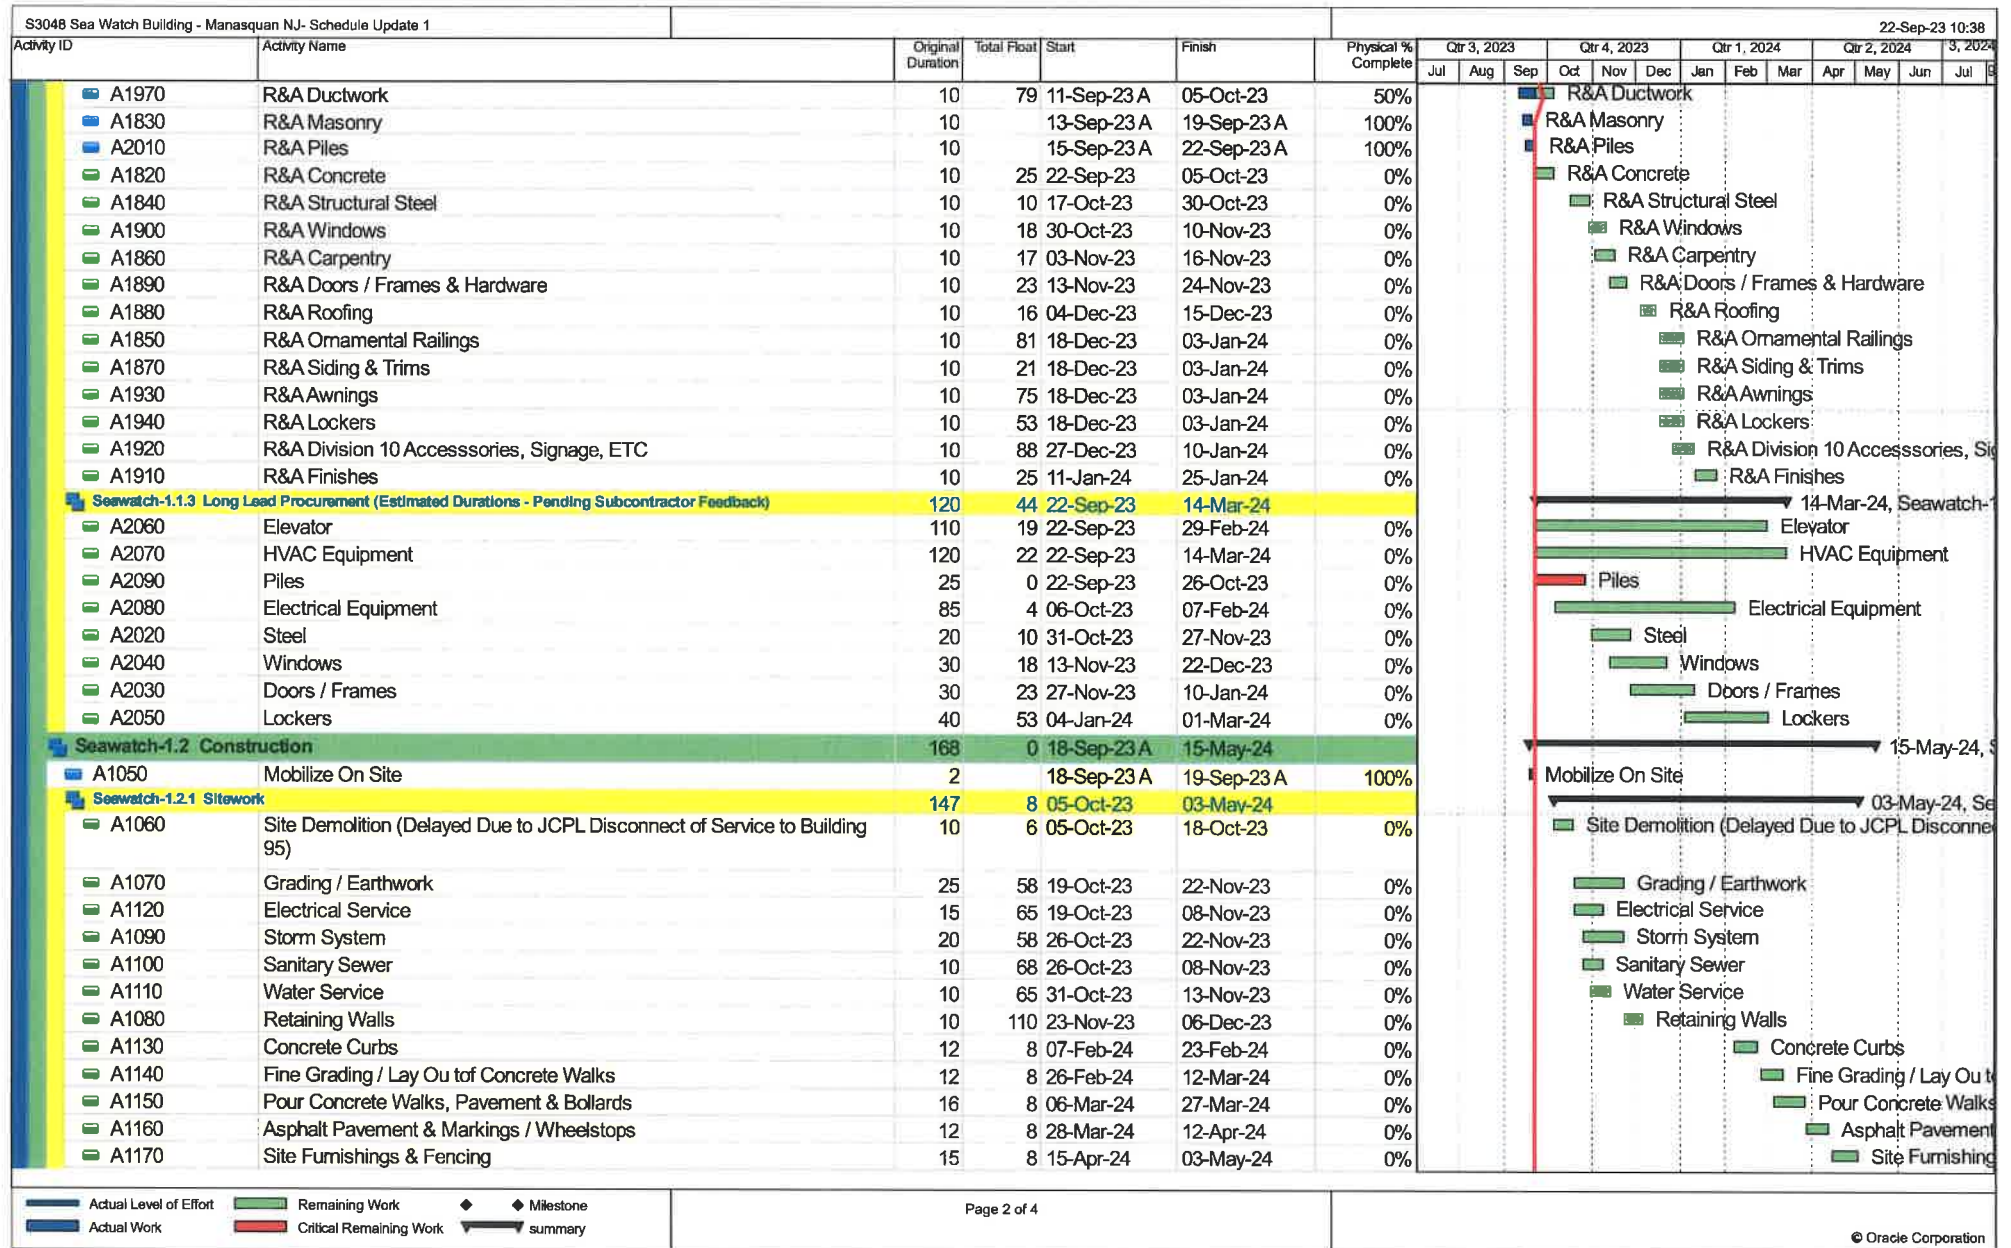

S3048 Sea Watch Building - Manasquan NJ- Schedule Update 1						22-Sep-23 10:38																	
Activity ID	Activity Name	Original Duration	Total Float	Start	Finish	Physical % Complete	Qtr 3, 2023			Qtr 4, 2023			Qtr 1, 2024			Qtr 2, 2024			3, 2024				
							Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun		Jul			
Seawatch-1.2.2 Building Construction							139	0	27-Oct-23	15-May-24													
A1180	Install Timber Piles	10	0	27-Oct-23	09-Nov-23	0%	Install Timber Piles																
A1190	Pile Testing / QC/QA	5	134	27-Oct-23	02-Nov-23	0%	Pile Testing / QC/QA																
A1200	Concrete Elevator Pit	12	0	10-Nov-23	27-Nov-23	0%	Concrete Elevator Pit																
A1210	Masonry Elevator Shaft	10	0	28-Nov-23	11-Dec-23	0%	Masonry Elevator Shaft																
A1810	Slab on Grade & Stair Piers	10	0	28-Nov-23	11-Dec-23	0%	Slab on Grade & Stair Piers																
A1230	Structure Framing	10	0	12-Dec-23	27-Dec-23	0%	Structure Framing																
A1350	Structural Steel & Decking	10	0	12-Dec-23	27-Dec-23	0%	Structural Steel & Decking																
A1270	Sheathing	8	1	28-Dec-23	09-Jan-24	0%	Sheathing																
A2140	Self Leveling Concrete @ Floor Deck	3	0	28-Dec-23	02-Jan-24	0%	Self Leveling Concrete @ Floor Deck																
A1240	Partition Framing	15	0	29-Dec-23	22-Jan-24	0%	Partition Framing																
A1280	Weather Barrier	7	1	02-Jan-24	10-Jan-24	0%	Weather Barrier																
A1600	Trex Decking, Water Management System	10	67	10-Jan-24	24-Jan-24	0%	Trex Decking, Water Management System																
A1290	Roofing	12	1	11-Jan-24	29-Jan-24	0%	Roofing																
A1310	Install Windows	8	8	11-Jan-24	23-Jan-24	0%	Install Windows																
A1490	Exterior Doors, Shutters & Vents	8	23	11-Jan-24	23-Jan-24	0%	Exterior Doors, Shutters & Vents																
A2150	Spray Foam Insulation, Batt Insulation	5	30	11-Jan-24	18-Jan-24	0%	Spray Foam Insulation, Batt Insulation																
A1480	Spray Foam Insulation	6	0	23-Jan-24	30-Jan-24	0%	Spray Foam Insulation																
A1300	Siding & Trim	20	8	24-Jan-24	21-Feb-24	0%	Siding & Trim																
A1370	Trex Decking & Water Management System	30	34	30-Jan-24	12-Mar-24	0%	Trex Decking & Water Management System																
A1260	Plumbing Rough In	15	0	31-Jan-24	21-Feb-24	0%	Plumbing Rough In																
A1320	Rough In Ductwork	15	0	31-Jan-24	21-Feb-24	0%	Rough In Ductwork																
A1590	Electrical Panels & Perm Power	10	4	08-Feb-24	22-Feb-24	0%	Electrical Panels & Perm Power																
A1330	Duct Insulation	7	0	22-Feb-24	01-Mar-24	0%	Duct Insulation																
A1340	Plumbing Insulation	7	0	22-Feb-24	01-Mar-24	0%	Plumbing Insulation																
A1250	Electrical Rough In	20	4	23-Feb-24	21-Mar-24	0%	Electrical Rough In																
A1360	Sheetrock T&S	15	0	04-Mar-24	22-Mar-24	0%	Sheetrock T&S																
A1380	Exterior Railings	12	34	13-Mar-24	28-Mar-24	0%	Exterior Railings																
A1470	HVAC Equipment	12	22	15-Mar-24	01-Apr-24	0%	HVAC Equipment																
A1220	Install Elevator	30	4	22-Mar-24	02-May-24	0%	Install Elevator																
A1400	Painting	8	0	25-Mar-24	03-Apr-24	0%	Painting																
A1410	Install Light Fixtures	15	10	04-Apr-24	24-Apr-24	0%	Install Light Fixtures																
A1420	Wiring Devices	15	5	04-Apr-24	24-Apr-24	0%	Wiring Devices																
A1430	Fire Alarm Devices	15	5	04-Apr-24	24-Apr-24	0%	Fire Alarm Devices																
A1440	Registers, Diffusers & Grilles	6	14	04-Apr-24	11-Apr-24	0%	Registers, Diffusers & Grilles																
A1460	Floor Finishes	12	0	04-Apr-24	19-Apr-24	0%	Floor Finishes																
A1520	Plumbing Equipment	10	2	04-Apr-24	17-Apr-24	0%	Plumbing Equipment																
A1500	Division 10 Lockers, Signage, Toilet Acc. ETC	10	5	15-Apr-24	26-Apr-24	0%	Division 10 Lockers, Signage, Toilet Acc. ETC																
A1450	Plumbing Fixtures	10	0	22-Apr-24	03-May-24	0%	Plumbing Fixtures																
A1510	Casework / Interior Wood Paneling & Trim	6	0	22-Apr-24	29-Apr-24	0%	Casework / Interior Wood Paneling & Trim																

Actual Level of Effort

Actual Work

Remaining Work

Critical Remaining Work

Milestone

summary

Page 3 of 4

© Oracle Corporation

Actual Level of Effort
 Remaining Work
 Milestone
 Critical Remaining Work
 summary

S3046 Sea Watch Building - Manasquan NJ- Schedule Update 1							22-Sep-23 10:38												
Activity ID	Activity Name	Original Duration	Total Float	Start	Finish	Physical % Complete	Qtr 3, 2023			Qtr 4, 2023			Qtr 1, 2024			Qtr 2, 2024			3, 2024
							Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul
A2160	Install Interior Doors	5	8	22-Apr-24	26-Apr-24	0%													Install Interior D
A2170	Casework, Interior Wood Paneling & Trim	10	3	22-Apr-24	03-May-24	0%													Casework, Inte
A1390	FRP & Stainless Steel Wall Paneling	12	0	30-Apr-24	15-May-24	0%													FRP & Stain
Seawatch-1.3 Close Out		15	0	25-Apr-24	15-May-24														15-May-24, S
A1530	Start Up Equipment & Testing	10	5	25-Apr-24	08-May-24	0%													Start Up Equi
A1540	Fire Alarm Testing	10	5	25-Apr-24	08-May-24	0%													Fire Alarm Tes
A1580	As-Built	5	8	29-Apr-24	03-May-24	0%													As-Built
A1550	Punchlist	5	3	06-May-24	10-May-24	0%													Punchlist
A1560	O&M Manuals	3	0	06-May-24	08-May-24	0%													O&M Manual
A1570	Owners Training	5	0	09-May-24	15-May-24	0%													Owners Train
